

# **PICEANCE HL NAD 83**

**RG 24-01S-098W**

**RGU 31-24-198 Pad**

**Federal RGU 332-24-198 - Slot A9**

**Wellbore #1**

**Plan: Plan #1 09Jan09 kjs**

## **Standard Planning Report - Geographic**

**06 April, 2010**

**Williams**  
Planning Report - Geographic

<b>Database:</b>	Compass R5000 WIN AUTH	<b>Local Co-ordinate Reference:</b>	Well Federal RGU 332-24-198 (A9) - Slot A9
<b>Company:</b>	PICEANCE HL NAD 83	<b>TVD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jib)
<b>Project:</b>	RG 24-01S-098W	<b>MD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jib)
<b>Site:</b>	RGU 31-24-198 Pad	<b>North Reference:</b>	True
<b>Well:</b>	Federal RGU 332-24-198	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Plan #1 09Jan09 kjs		

<b>Project</b>	RG 24-01S-098W, Rio Blanco County, CO, RG 24-01S-098W		
<b>Map System:</b>	US State Plane 1983	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	North American Datum 1983		
<b>Map Zone:</b>	Colorado Central Zone		

Site		RGU 31-24-198 Pad			
Site Position:		Northing:	1,784,364.83 usft	Latitude:	39° 57' 9.910 N
From:	Map	Easting:	2,204,117.18 usft	Longitude:	108° 20' 20.975 W
Position Uncertainty:	0.0 usft	Slot Radius:	0.000 in	Grid Convergence:	-1.791 °

Well	Federal RGU 332-24-198 - Slot A9					
Well Position	+N/-S	0.0 usft	Northing:	1,784,356.00 usft	Latitude:	39° 57' 9.786 N
	+E/-W	0.0 usft	Easting:	2,203,997.40 usft	Longitude:	108° 20' 22.508 W
Position Uncertainty		0.0 usft	Wellhead Elevation:		Ground Level:	6,544.0 usft

<b>Wellbore</b>	Wellbore #1				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	IGRF200510	1/8/2009	10.862	66.126	52,718

<b>Design</b>	Plan #1 09Jan09 kjs				
<b>Audit Notes:</b>					
<b>Version:</b>		<b>Phase:</b>	PLAN	<b>Tie On Depth:</b>	0.0
<b>Vertical Section:</b>	<b>Depth From (TVD) (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Direction (°)</b>	
	0.0	0.0	0.0	195.82	

<b>Plan Sections</b>										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.000	
120.0	0.00	0.00	120.0	0.0	0.0	0.00	0.00	0.00	0.000	
319.9	4.00	195.82	319.7	-6.7	-1.9	2.00	2.00	0.00	195.816	
7,616.6	4.00	195.82	7,598.7	-496.2	-140.6	0.00	0.00	0.00	0.000	
7,883.1	0.00	0.00	7,865.0	-505.1	-143.1	1.50	-1.50	0.00	180.000	Mesaverde (25' Radiu
12,753.1	0.00	0.00	12,735.0	-505.1	-143.1	0.00	0.00	0.00	0.000	

**Williams**  
Planning Report - Geographic

<b>Database:</b>	Compass R5000 WIN AUTH	<b>Local Co-ordinate Reference:</b>	Well Federal RGU 332-24-198 (A9) - Slot A9
<b>Company:</b>	PICEANCE HL NAD 83	<b>TVD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jjb)
<b>Project:</b>	RG 24-01S-098W	<b>MD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jjb)
<b>Site:</b>	RGU 31-24-198 Pad	<b>North Reference:</b>	True
<b>Well:</b>	Federal RGU 332-24-198	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Plan #1 09Jan09 kjs		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
0.0	0.00	0.00	0.0	0.0	0.0	1,784,356.00	2,203,997.40	39° 57' 9.786 N	108° 20' 22.508 W
120.0	0.00	0.00	120.0	0.0	0.0	1,784,356.00	2,203,997.40	39° 57' 9.786 N	108° 20' 22.508 W
319.9	4.00	195.82	319.7	-6.7	-1.9	1,784,349.36	2,203,995.29	39° 57' 9.719 N	108° 20' 22.533 W
7,616.6	4.00	195.82	7,598.7	-496.2	-140.6	1,783,864.46	2,203,841.41	39° 57' 4.882 N	108° 20' 24.313 W
7,883.1	0.00	0.00	7,865.0	-505.1	-143.1	1,783,855.60	2,203,838.60	39° 57' 4.794 N	108° 20' 24.345 W
12,753.1	0.00	0.00	12,735.0	-505.1	-143.1	1,783,855.60	2,203,838.60	39° 57' 4.794 N	108° 20' 24.345 W

Design Targets									
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
Mesaverde (25' Radius) - plan hits target center - Circle (radius 25.0)	0.00	0.00	7,865.0	-505.1	-143.1	1,783,855.60	2,203,838.60	39° 57' 4.794 N	108° 20' 24.345 W
Mesaverde (50' Radius) - plan hits target center - Circle (radius 50.0)	0.00	0.00	7,865.0	-505.1	-143.1	1,783,855.60	2,203,838.60	39° 57' 4.794 N	108° 20' 24.345 W


Casing Points					
Measured Depth (usft)	Vertical Depth (usft)	Name	Casing Diameter (in)	Hole Diameter (in)	
3,863.0	3,854.2	9 5/8"	9.625	13.500	

**Williams**  
Planning Report - Geographic



<b>Database:</b>	Compass R5000 WIN AUTH	<b>Local Co-ordinate Reference:</b>	Well Federal RGU 332-24-198 (A9) - Slot A9
<b>Company:</b>	PICEANCE HL NAD 83	<b>TVD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jjb)
<b>Project:</b>	RG 24-01S-098W	<b>MD Reference:</b>	KELLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jjb)
<b>Site:</b>	RGU 31-24-198 Pad	<b>North Reference:</b>	True
<b>Well:</b>	Federal RGU 332-24-198	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Plan #1 09Jan09 kjs		

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
1,157.2	1,155.0	Green River Fm				
1,357.7	1,355.0	A Groove				
1,578.2	1,575.0	B Groove				
1,879.0	1,875.0	Dissolution Surface				
2,966.6	2,960.0	Garden Gulch				
3,142.0	3,135.0	Orange Marker				
3,362.6	3,355.0	Wasatch				
5,808.5	5,795.0	G' Sand				
6,199.5	6,185.0	Ft. Union				
7,562.8	7,545.0	Ohio Creek				
7,883.1	7,865.0	Mesaverde				
9,563.1	9,545.0	Top Gas				
11,148.1	11,130.0	Cameo Coals				
11,553.1	11,535.0	Rollins SS				
11,688.1	11,670.0	Cozzette				
11,893.1	11,875.0	Corcoran				
12,278.1	12,260.0	Upper Sego				
12,503.1	12,485.0	Lower Sego				
12,753.1	12,735.0	TD		0.000		

Plan Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
120.0	120.0	0.0	0.0	Start Build 2.00
319.9	319.7	-6.7	-1.9	Hold 4 Inc
7,616.6	7,598.7	-496.2	-140.6	Start Drop -1.50
7,883.1	7,865.0	-505.1	-143.1	Vertical
12,753.1	12,735.0	-505.1	-143.1	TD at 12753.1

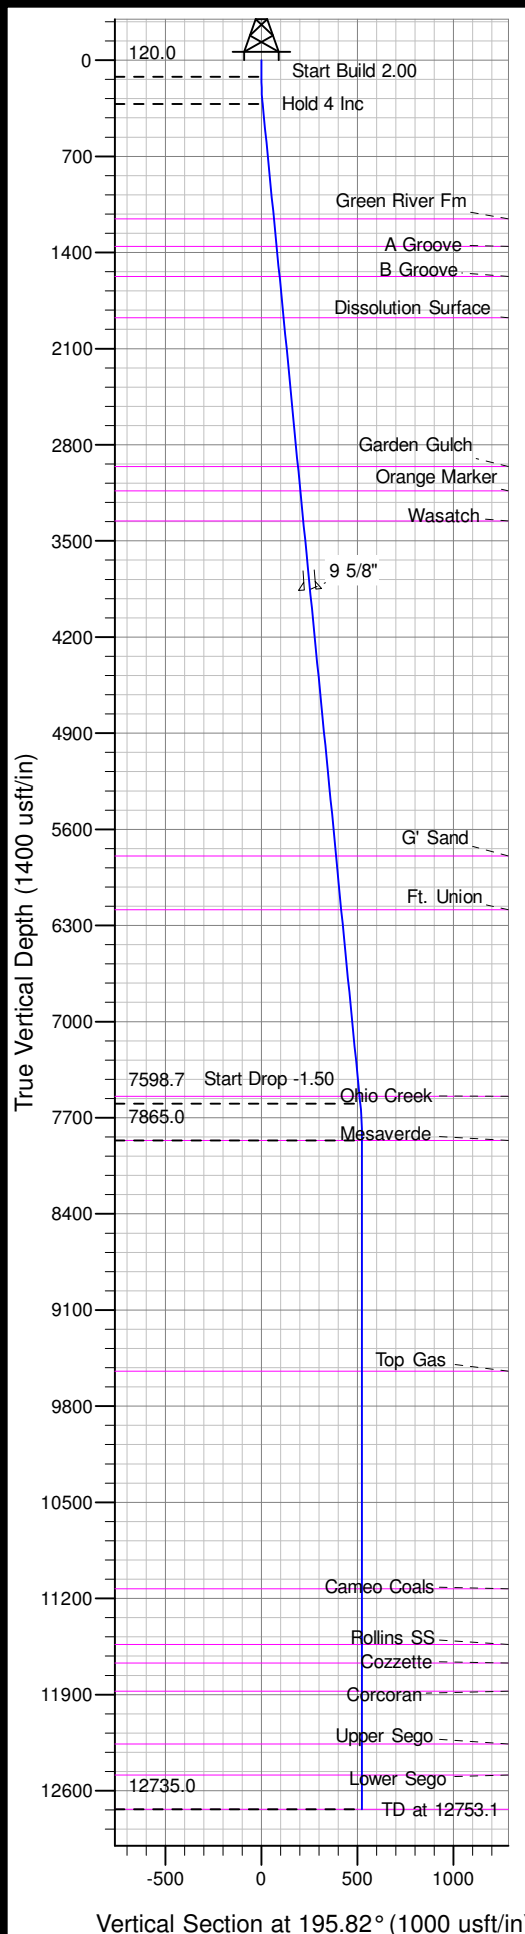

Well Name: Federal RGU 332-24-198  
 Surface Location: RGU 31-24-198 Pad  
 North American Datum 1983 US State Plane 1983 Colorado Central Zone  
 Ground Elevation: 6544.0  
 +N/-S +E/-W Northing Easting Latitude Longitude Slot  
 0.0 0.0 1784356.00 2203997.40 39° 57' 9.786 N 108° 20' 22.508 W A9  
 Cyclone 29 (21' RKB) KJLY BUSHING @ 6565.0usft (Cyclone 29 (21' RKB) jib)

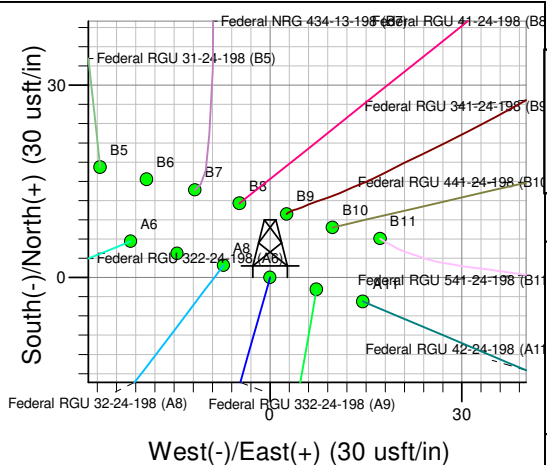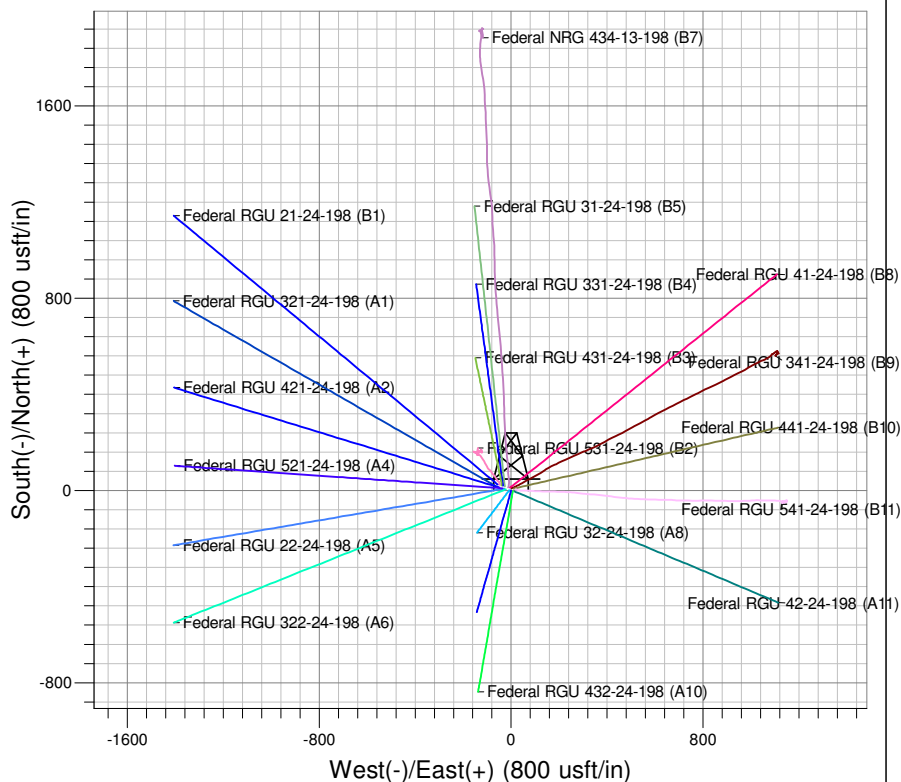

Project: RG 24-01S-098W  
 Site: RGU 31-24-198 Pad  
 Well: Federal RGU 332-24-198  
 Plan: Plan #1 09Jan09 kjs

Azimuths to True North  
 Magnetic North: 10.86°  
 Magnetic Field  
 Strength: 52718.3snT  
 Dip Angle: 66.13°  
 Date: 1/8/2009  
 Model: IGRF200510

#### SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.000	0.0	
120.0	0.00	0.00	120.0	0.0	0.0	0.00	0.000	0.0	
319.9	4.00	195.82	319.7	-6.7	-1.9	2.00	195.816	7.0	
7616.6	4.00	195.82	7598.7	-496.2	-140.6	0.00	0.000	515.7	
7883.1	0.00	0.00	7865.0	-505.1	-143.1	1.50	180.000	525.0	Mesaverde (25' Radius) Federal RGU 332-24-198
2753.1	0.00	0.00	12735.0	-505.1	-143.1	0.00	0.000	525.0	

TVD	MD	Inc	Azi	+N/-S	+E/-W	VSect	Departure	Annotation
120.0	120.0	0.00	0.00	0.0	0.0	0.0	0.0	Start Build 2.00
319.7	319.9	4.00	195.82	-6.7	-1.9	7.0	7.0	Hold 4 Inc
7598.7	7616.6	4.00	195.82	-496.2	-140.6	515.7	515.7	Start Drop -1.50
7865.0	7883.1	0.00	0.00	-505.1	-143.1	525.0	525.0	Vertical
12735.0	12753.1	0.00	0.00	-505.1	-143.1	525.0	525.0	TD at 12753.1
