



Krabacher, Jay

**To:** Barber, Matt  
**Cc:** Andrews, David; King, Kevin  
**Subject:** RE: Jolley KP 423-8 - Request to defer CBL (045-20996)

Matt:

WPX can delay the CBL on this well.

Is the bradenhead continuing to require mud/fluid to keep the well filled to surface?

Regards,

Jay Krabacher

---

**From:** Barber, Matt [<mailto:Matthew.Barber@wpxenergy.com>]  
**Sent:** Thursday, April 19, 2012 10:37 AM  
**To:** King, Kevin  
**Cc:** Andrews, David; Krabacher, Jay  
**Subject:** Jolley KP 423-8 - Request to defer CBL

Hey Kevin:

WPX Energy Rocky Mountain, LLC requests a CBL deferment on the Jolley KP 423-8 located in the SESW of Section 8, T6S-R91W. Attached is a temperature survey that was performed after cementing the 4 ½" production casing on the subject well. Also, attached is a bradenhead pressure summary.

Information pertaining to the request is as follows:

Well:	Jolley KP 423-8
API:	05-045-20996-00
Location:	SESW, Section 8, T6S-R91W
Surface Csg:	9 5/8" set and cemented at 1,349'
Production Csg Cement Date:	4 ½" @ 7,559' – cemented 04/05/2012
Cement:	1,130sks
Cement top from survey:	2,400' (Estimated)
Estimated top of gas:	4,625'
Temp Survey:	Attached
Volume to fill annular:	Hole remained full following cementing operations


Please let me know if you need additional information to approve this deferment. After deferment is received, WPX will continue to monitor the bradenhead pressure until CBL is run and notify if pressure exceeds 150 psig.

Thank you,


Matt

Matt Barber  
Sr. Regulatory Specialist

**RECEIVED**  
**APR 19 2012**  
**COGCC/Rifle Office**

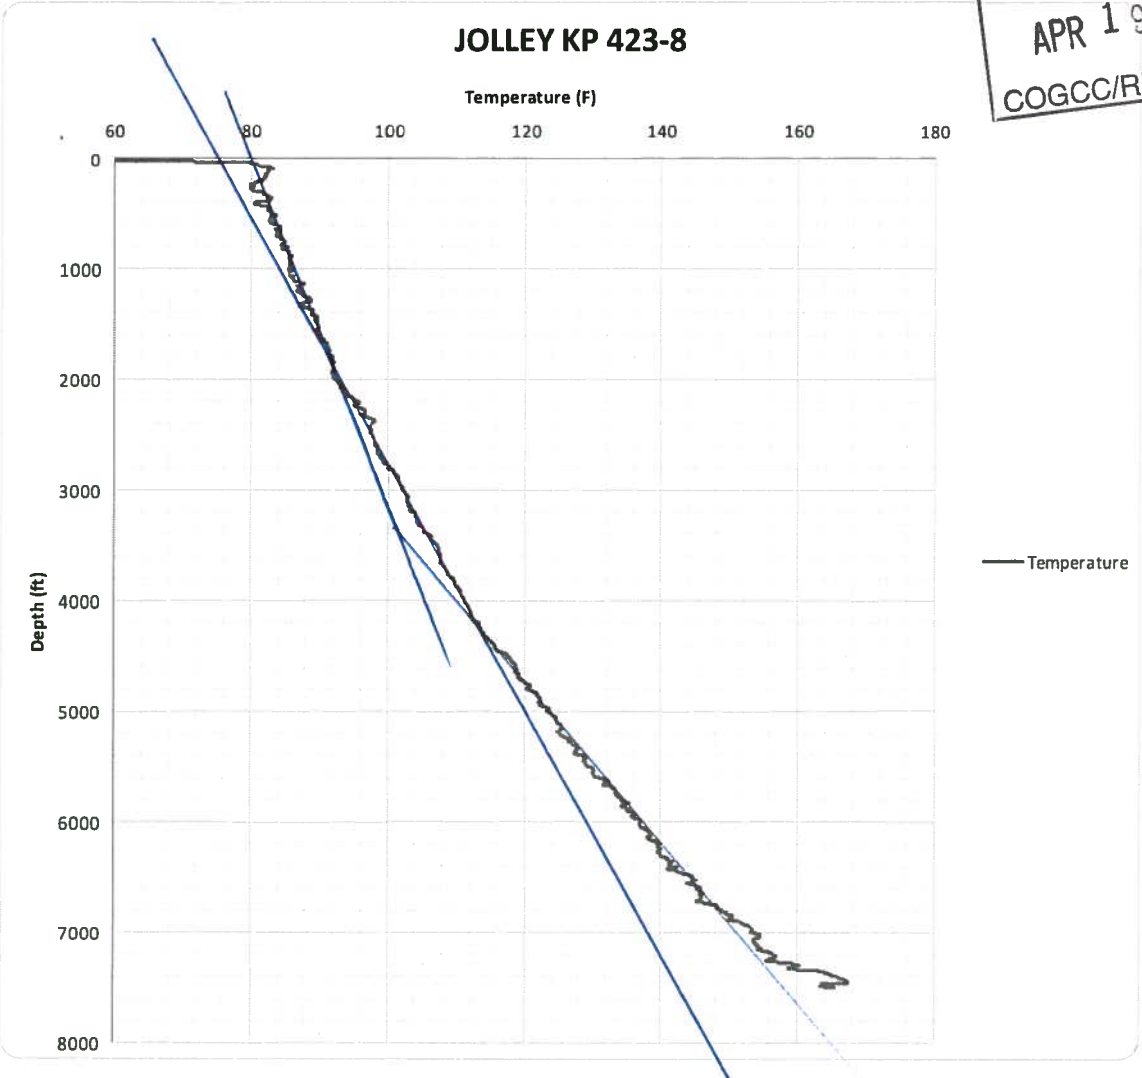

## Bradenhead Pressure Summary



WELL: Jolley KP 423-8

LOCATION: SE/4SW/4 SEC. 8 T6S-R91W 6<sup>TH</sup> PM

API#: 05-045-20996-00

TEMP. LOG RUN DATE: 04/14/2012

TOP OF CEMENT: 2400' (Est.)

TOP OF GAS: 4625'

### **BRADENHEAD PRESSURES (psig)**

WELLHEAD PRESSURE Jolley KP 423-8

4/14/2012	11:00	6 HR	4 BBLS TO FILL	0 PSI
4/14/2012	17:00	12 HR	0 BBLS TO FILL	0 PSI
4/15/2012	05:00	24 HR	0 BBLS TO FILL	0 PSI
4/16/2012	05:00	48 HR	2 BBLS TO FILL	0 PSI
4/17/2012	05:00	72 HR	5 BBLS TO FILL	0 PSI
