


Confluence DJ LLC  
70 Ranch 10-8-2L  
Producing Fm: Niobrara B  
05-123-46619  
SWSW Sec 3-4N-63W  
Weld County, CO

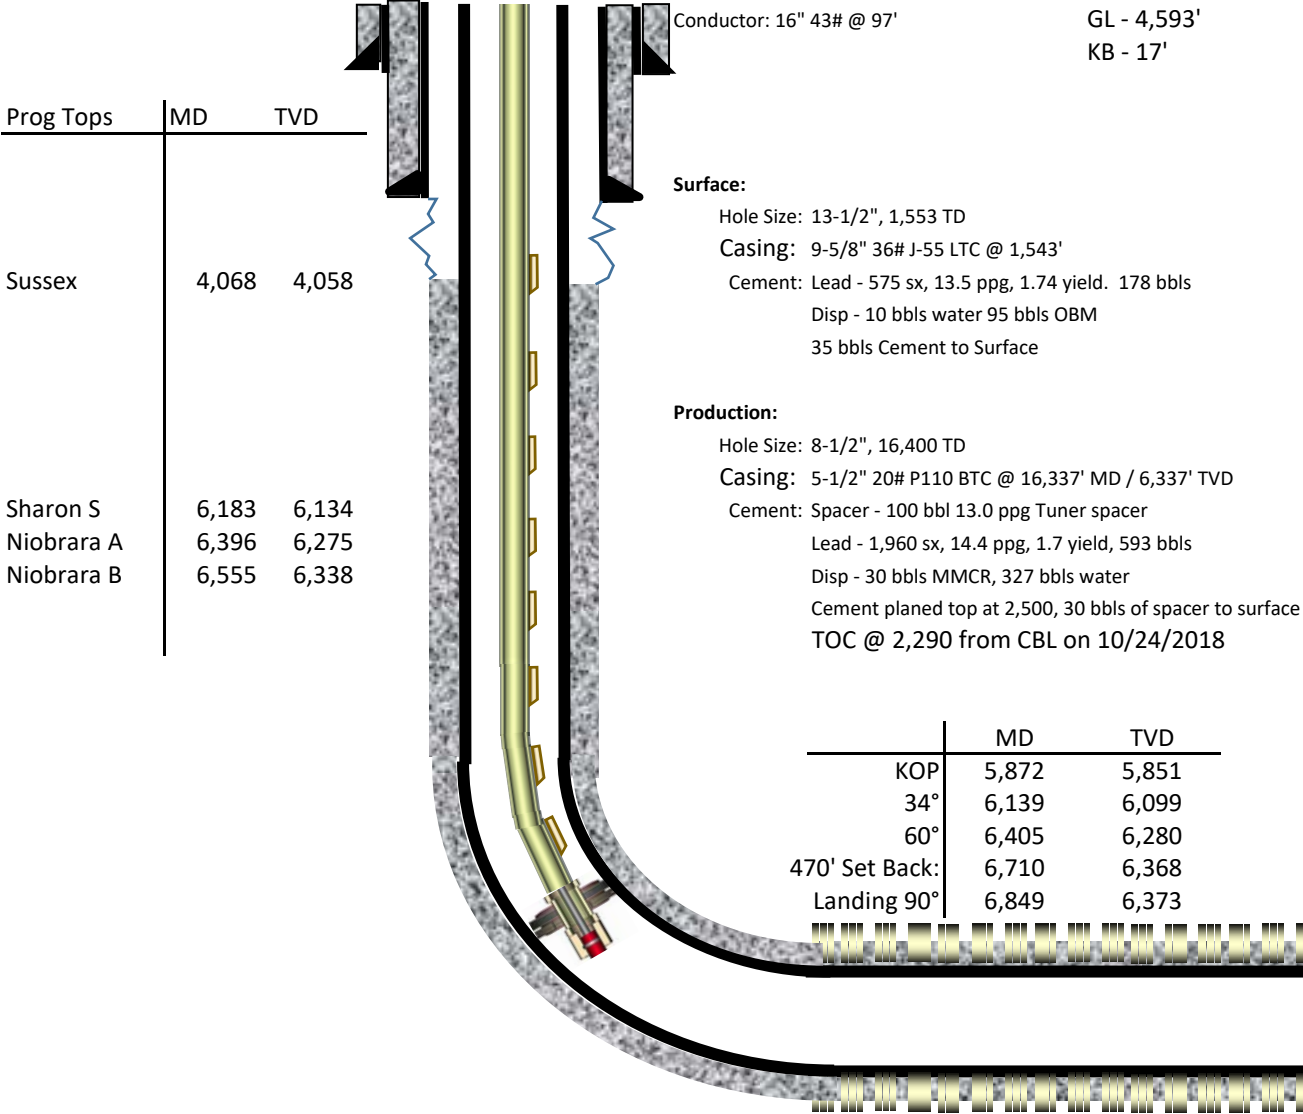

Tubing String	Length	Running	Approx Inc
KB to top of tubing	17	17	
Tubing Hanger	0.5	17.50	
1 jt 2-3/8" tbg		17.50	
XX jt 2-3/8" tbg sub (4', 6', 8')		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #8		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #7		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #6		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #5		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #4		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #3		17.50	
x jt 2-3/8" tbg		17.50	
FlowCo Gas Lift Valve #2		17.50	
x jt 2-3/8" tbg		17.50	
X Nipple 1.875" ID		17.50	
1 jt 2-3/8" tbg		17.50	
Flowco Gas Lift Oriffice Mandrel #1 - 16/64		17.50	
1 jt 2-3/8" tbg		17.50	
5-1/2' x 2-3/8" On-off Tool		17.50	
2.62" x 1.875" stinger nipple		17.50	
AS1-X 2-3/8" x 5-1/2" Packer, 4.62" OD, 2" ID		17.50	
Pump out Plug in 2-3/8" Perf Sub w/ bull nose		17.50	
		17.50	
EOT	17.50		

	Float Sub	ORIO III	Float Collar	Float Shoe	TD
MD (ft):	5,806	16,325	16,373	16,387	16,400
TVD (ft):	5,785	6,337	6,337	6,337	6,337

Frac Summary: 60 Stages, 17,001,420 total lbs sand & 373,775 bbls fluid. Ave Rate 77.4 bpm, Ave PSI 5,648, Max PSI 7,144
