



# DOMINION ENERGY

***F WILSON 8***

***REMEDIAL***

***PTA***

***MOFFATT COUNTY***

## NOTICE

THIS PROPOSAL IS GOOD FOR A PERIOD OF 30 DAYS FROM THE DATE OF ISSUE. THE INFORMATION INCLUDED IN THIS PROPOSAL IS PRESENTED IN GOOD FAITH, AND PRICES QUOTED ARE ESTIMATES ONLY BASED ON THE FACTS PROVIDED BY OTHERS. NO WARRANTY IS MADE CONCERNING THE ACCURACY OR COMPLETENESS OF DATA, INFORMATION PRESENTED, EFFECTIVENESS OF MATERIAL, PRODUCTS OR SUPPLIES, RECOMMENDATIONS MADE, OR THE RESULTS OF THE SERVICES PROVIDED. CERTAIN ITEMS ARE ESTIMATES ONLY, AND WILL VARY DEPENDING UPON THE DISTANCE TRAVELED, TIME, EQUIPMENT AND MATERIAL, ULTIMATELY REQUIRED TO PERFORM THESE SERVICES. THESE ITEMS THAT ARE SUBJECT TO VARY WILL BE BILLED BASED ON THE ACTUAL AMOUNTS INCURRED (i.e. MILEAGE, INCREASE IN MATERIALS). FREEDOM FROM INFRINGEMENT OF ANY INTELLECTUAL PROPERTY RIGHTS IS NOT TO BE INFERRED WITH RESPECT TO ANY MATERIAL INCLUDED IN THIS PROPOSAL AND NO INTELLECTUAL PROPERTY RIGHTS ARE GRANTED HEREBY.

### CEMENTING - ROCKY MOUNTAIN DIVISION

P.O. BOX 827 - VERNAL UT, 84078 - (435) 789-7407

COMPANY NAME: DOMINION

DATE: 7/1/2020

COUNTY: MOFFAT

LEASE NAME: F WILSON 8

RIG NO: D&D SWAB

DESCRIPTION	TIME	RATE	PSI	VOLUME
SAFTY MEETING SHOP	4:00			
ON LOC	7:45			
SAFTY MEETING RIG UP	8:30			
SAFTY MEETING DOG HOUSE	9:00			
PSI TEST PUMP & LINES	9:18	2	0-2000	0-2
CICR SET @ 1685' INJ RATE	9:21	1.5	0-920	0-10
START CMT @ 15.8	9:29	2	910	0
SHUT DOWN STING OUT 112.2 SKS	9:40	"	1340	23
MIXED 148 SKS				
DISP WHATS IN TUBING				
START DISP	9:42	3	70	0
END 47 SKS ONTOP CICR 240'		3	100	8
REVERSE	10:03	2	120	0
CMT BACK	10:08	"	150	10.5
CLEAR	10:08	"	140	11
END	10:09	"	140	13
MUD SPACER	10:15	3	150	0
END	10:18	"	150	9.9
DISP	10:18	"	150	0-6
EOT 1157' FILL HOLE	10:30	2	0-70	0-2
START CMT @ 15.8	10:37	3	150	0
END 30 SKS 126.2' PLUG	10:39	"	70	6.1
DISP	10:39	"	70	0
END	10:41	"	90	5.7
MUD SPACER TO SURFACE	10:54	3.5	280	0
END	11:05	"	260	38.5
TOOH SHOOT HOLES @ 340'				
TRY TO PUMP THROUGH HOLES	12:03	2.5	0-440	0-14 RETURNS
H2O	12:26	2	360	0-10
START DYE WATER	12:34	2.5	380	0-3
START CMT @ 15.8	12:36	"	400	0
END NEET CMT	12:41	"	330	12
CONTINUE CMT 1 % CACL	12:41	"	330	12
CMT TO SURFACE 170.8 SKS	12:50	"	210	35
SHUT DOWN WAIT 10 MIN	12:51	"	210	36
START CMT	13:05	0.7	140	36
END 205 SKS	13:13	"	130	42
WASH PUMP RIG/RIG DOWN				
DIG WELL UP				

OPERATOR: KARL CHAPMAN

ACCEPTED AND APPROVED BY:



# PROPETRO

## JOB LOG

**TICKER NUMBER: KC -383**

## CEMENTING - ROCKY MOUNTAIN DIVISION

**P.O. BOX 827 - VERNAL UT, 84078 - (435) 789-7407**

**COMPANY NAME: DOMINION ENERGY**

**DATE: 7/1/2020**

**COUNTY: MOFFAT**

**LEASE NAME: F WILSON 8**

**RIG NO: D&D SWABBING**[illegible]

**OPERATOR: KARL CHAPMAN**

**ACCEPTED AND APPROVED BY:**

**PROPETRO****JOB SUMMARY****TICKER NUMBER: KC-383****CEMENTING - ROCKY MOUNTAIN DIVISION**


P.O. BOX 827 - VERNAL UT, 84078 - (435) 789-7407

**COMPANY NAME: DOMINION****DATE: 7/1/2020****COUNTY: MOFFAT****LEASE NAME: F WILSON 8****RIG NO: D&D SWAB****JOB TYPE: PTA**


DESCRIPTION	WGT/GRADE	THREAD	DEPTH FROM	DEPTH TO
<b>SURFACE CSG SIZE: 10 3/4</b>	<b>N/A</b>		<b>0</b>	<b>N/A</b>
<b>INTER CSG SIZE:</b>				
<b>PROD CSG SIZE: 7</b>	<b>20</b>		<b>0</b>	<b>N/A</b>
<b>LINER CSG SIZE:</b>				
<b>TBG OR DP SIZE: 2 7/8</b>			<b>0</b>	<b>1685</b>
MATERIALS FURNISHED	SACKS	SLURRY WT PPG	SLURRY YIELD FT3	WATER GAL/SK
<b>PREM CMT (G)</b>	<b>385</b>	<b>15.8</b>	<b>1.15</b>	<b>5</b>
<b>POZ MIX 9# MUD</b>	<b>50 BBLS</b>	<b>9</b>		

**EQUIPMENT: 1372/902/66/17****PERSONELL: KARL/JAKE/DARRIN****NOTES: 383 SKS TOTAL CMT , CMT TO SURFACE put 2 sks of cmt on ground****OPERATOR: KARL CHAPMAN****ACCEPTED AND APPROVED BY:**

# DOMINION PTA

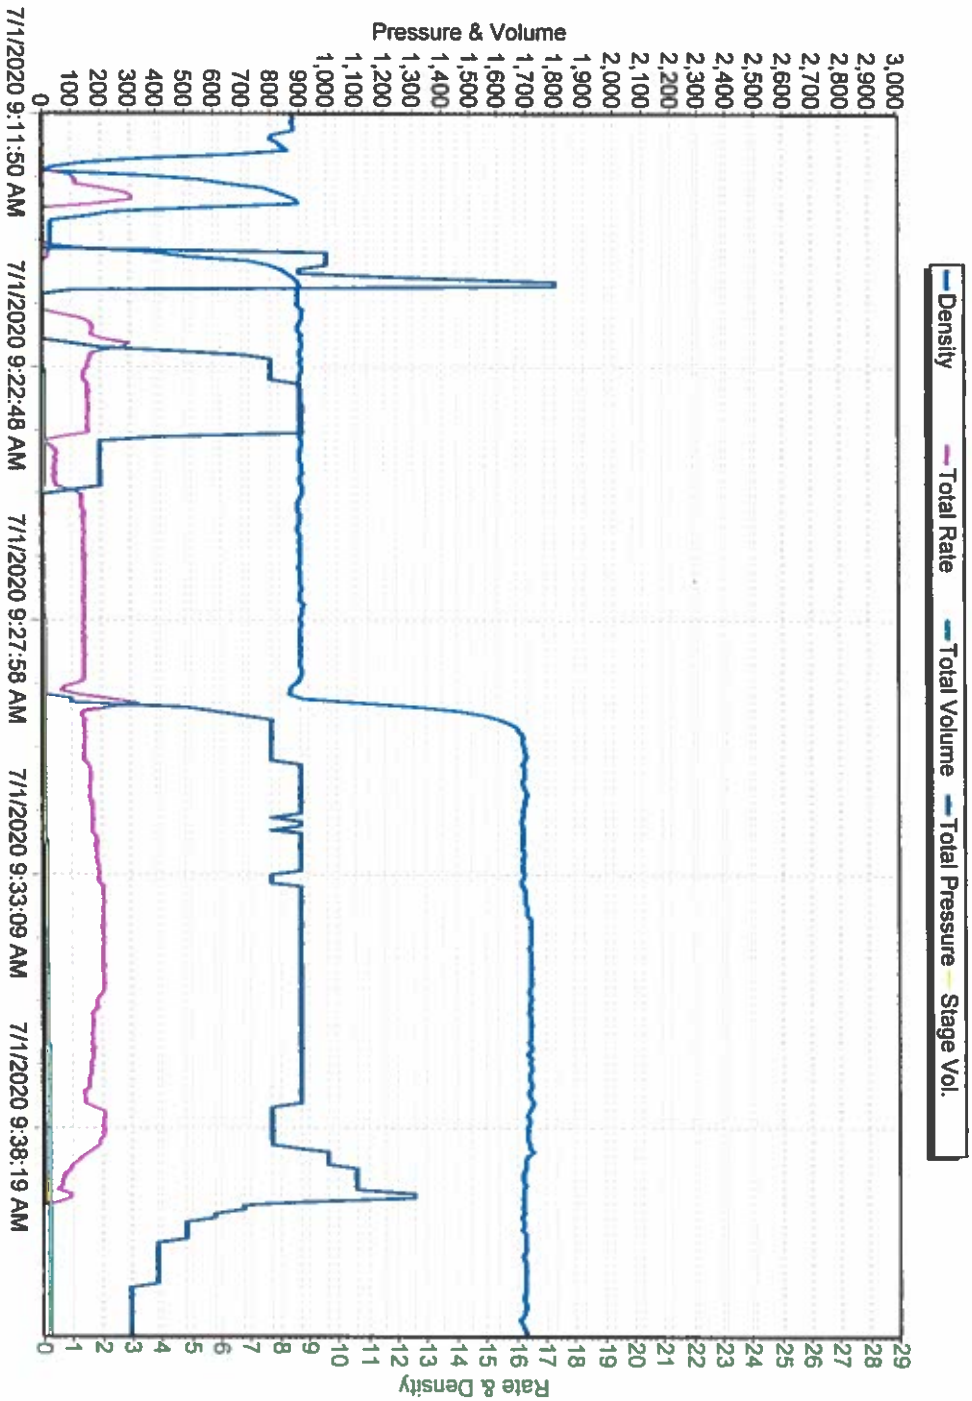


# DOMINION PTA

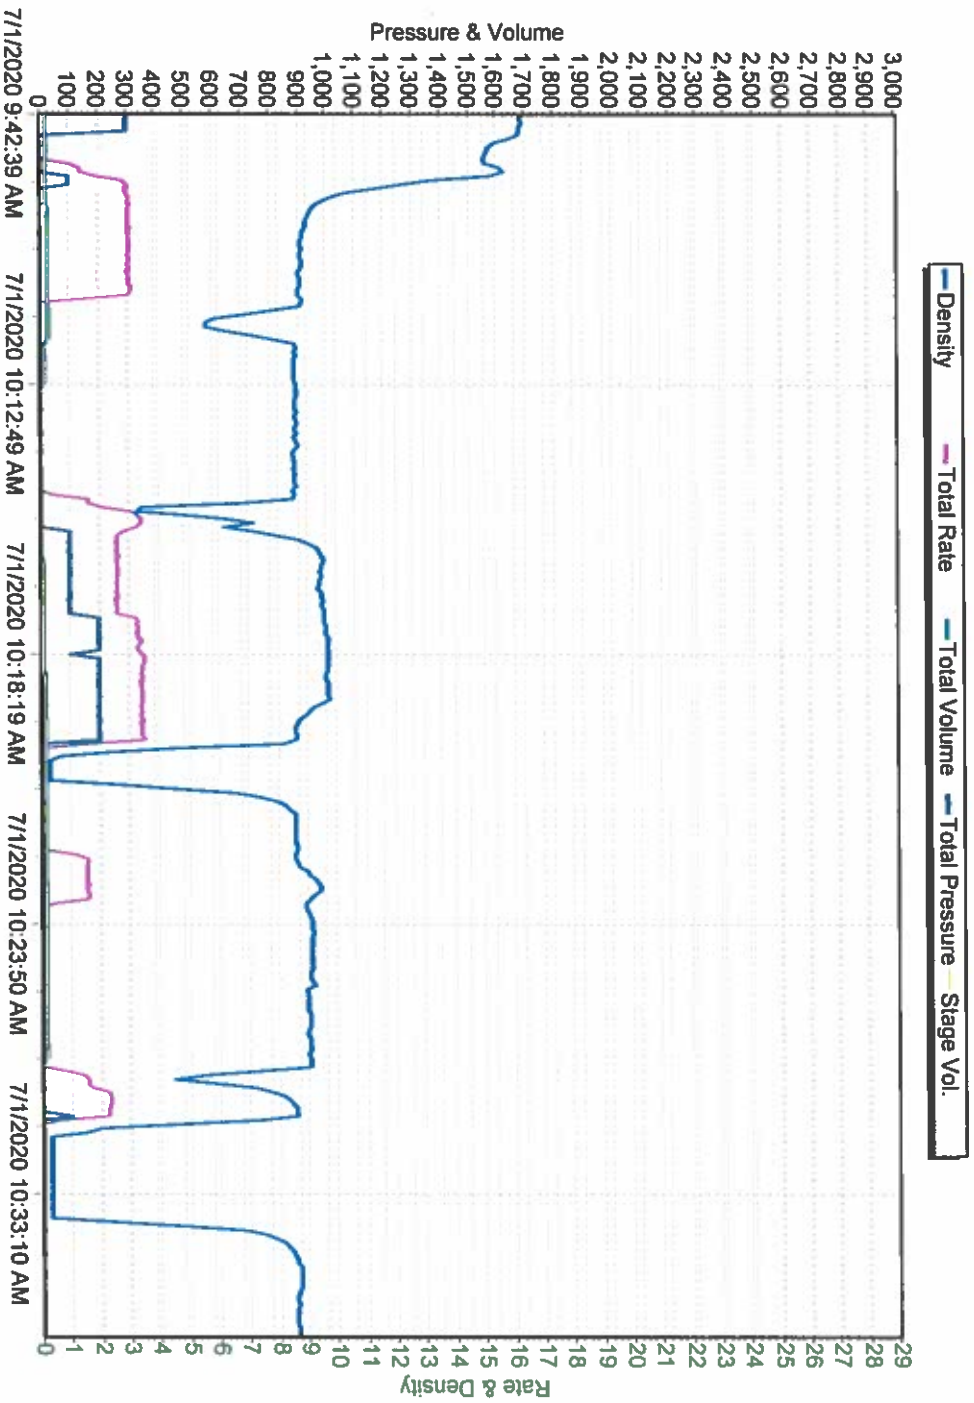




# DOMINION PTA

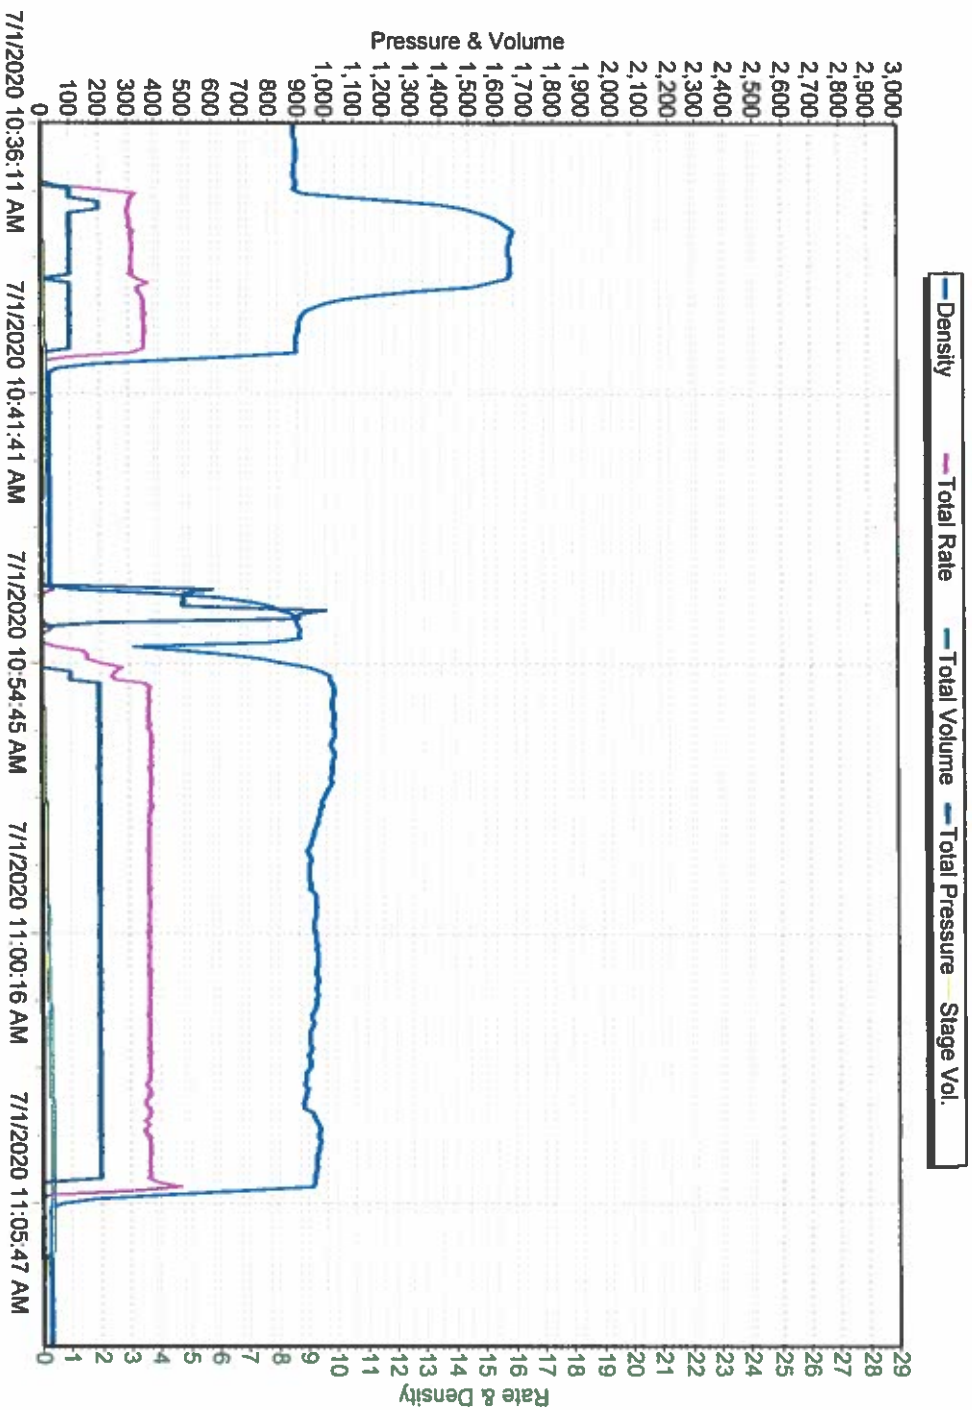

# DOMINION PTA

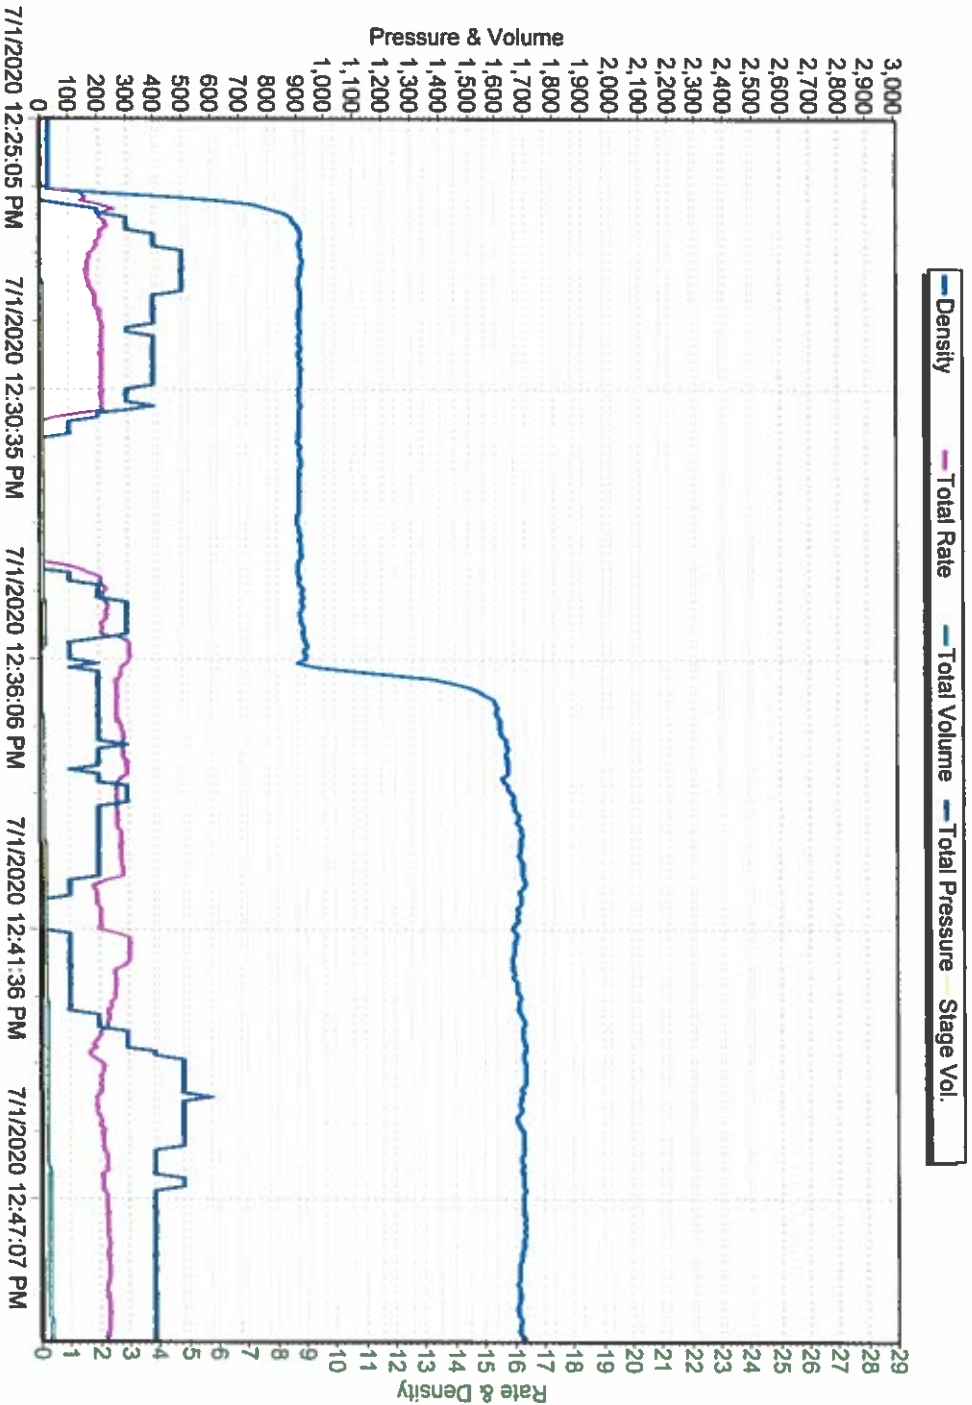



# DOMINION PTA

