


# Wall Plot

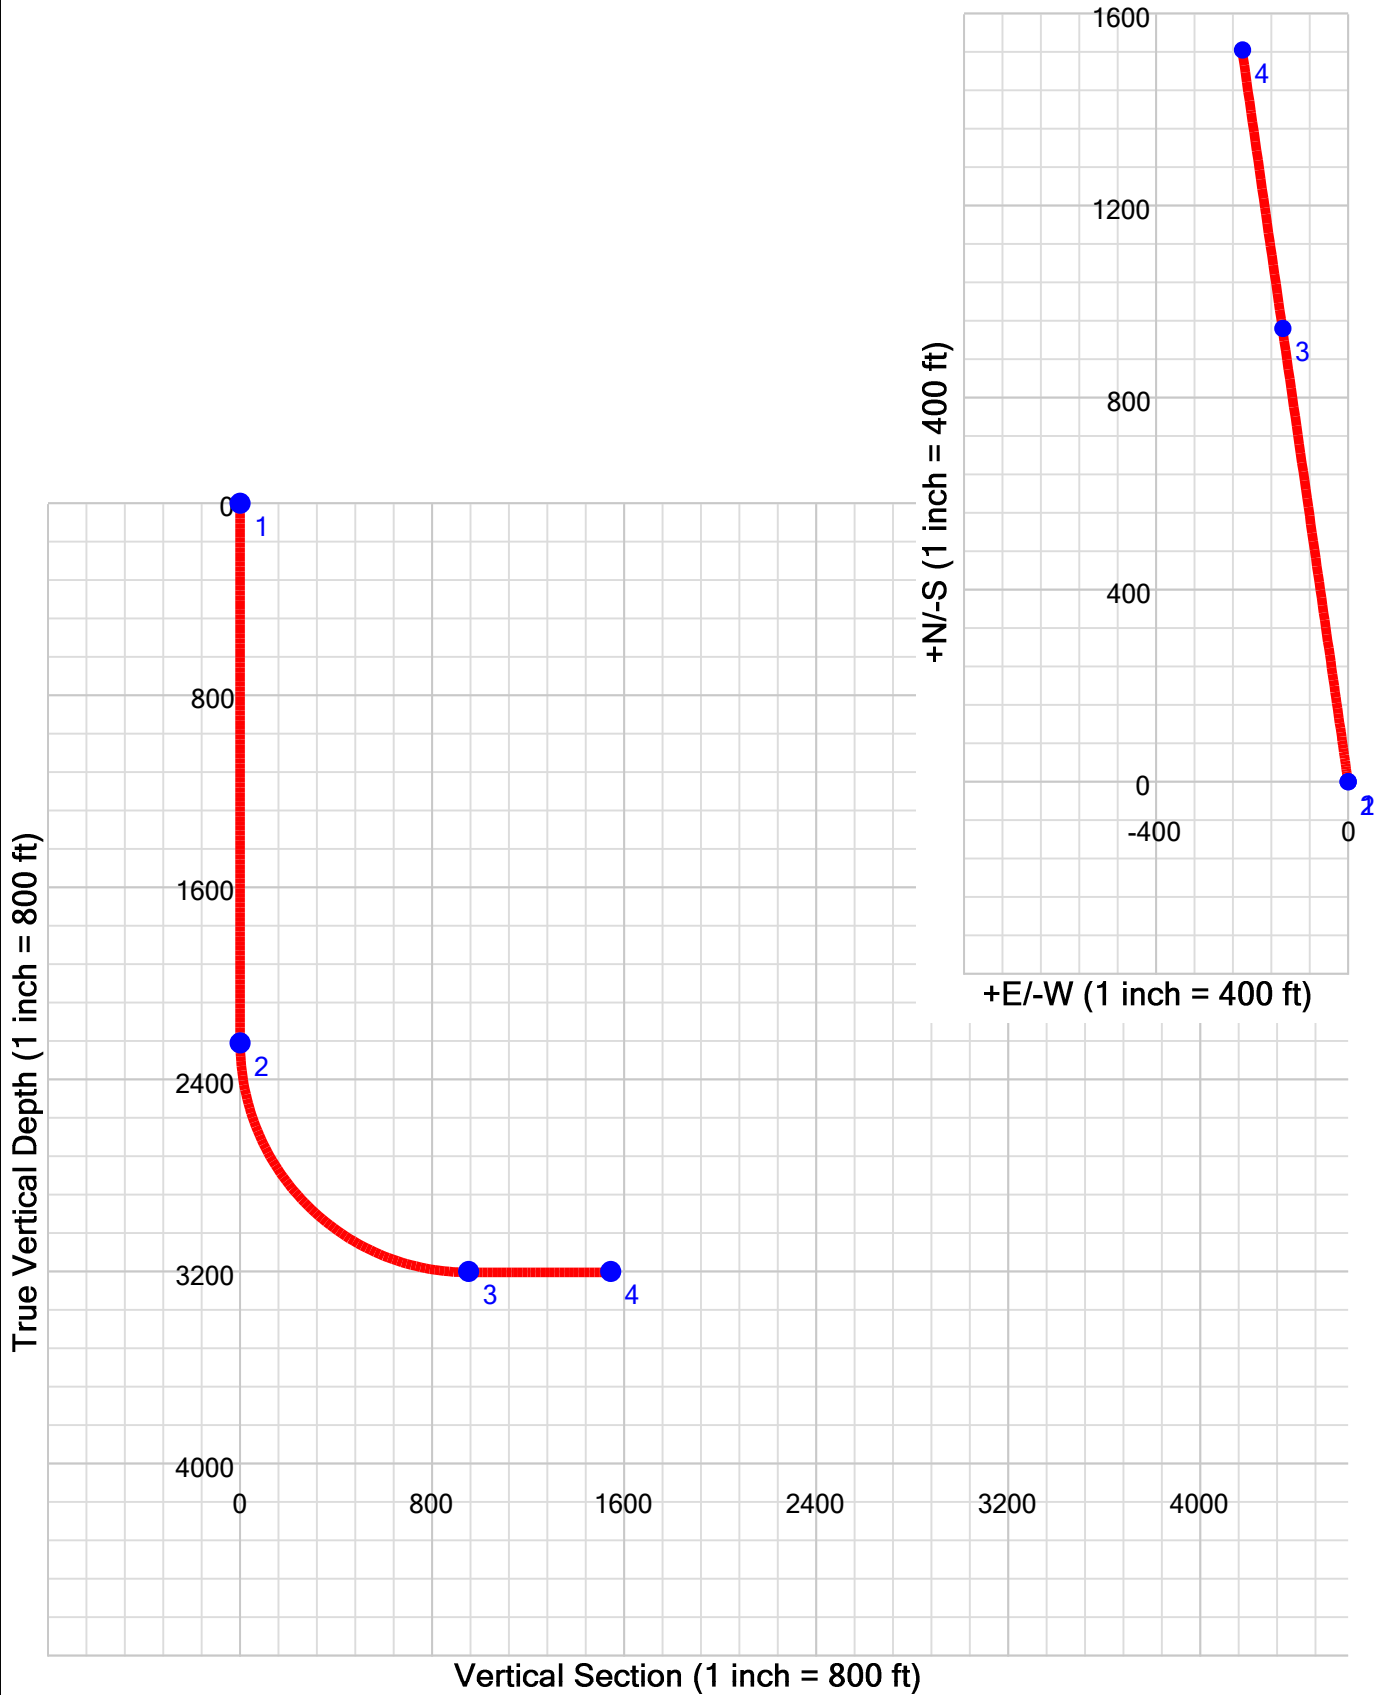

#	MD	Inc	Azi	TVD	+N/-S	+E/-W	DL	TFO	VS	Comments	Company:	PRO&G
1	0.0	0.00	351.75	0.0	0.0	0.0	0.00	0.00	0.0		Project:	Cutthroat 33-29_Ver 1
2	2245.1	0.00	351.75	2245.1	0.0	0.0	0.00	0.00	0.0	KOP	Well:	
3	3745.1	90.00	351.75	3200.1	945.0	-137.0	6.01	0.00	954.9	EOB	By:	Moe Felman
4	4331.1	90.00	351.75	3200.1	1524.9	-221.1	0.00	0.00	1540.9		Date:	4/22/2010
											Vertical section azimuth:	351.75°
											Survey calculation method:	Minimum Curvature
											Units:	Length - ft, Dogleg - °/100ft
