

The Road to Excellence Starts with Safety

The Road to Excellence Starts With Safety			
Sold To #: 300721	Ship To #: 2898356	Quote #:	Sales Order #: 9153019
Customer: WILLIAMS PRODUCTION RMT INC - EBUS		Customer Rep: BASCOM, BRENT	
Well Name: RWF		Well #: 511-32	API/UWI #: 05-045-21052
Field: Rulison	City (SAP): RIFLE	County/Parish: Garfield	State: Colorado
Lat: N 39.486 deg. OR N 39 deg. 29 min. 8.621 secs.		Long: W 107.916 deg. OR W -108 deg. 5 min. 3.116 secs.	
Contractor: CYCLONE 17		Rig/Platform Name/Num: CYCLONE 17	
Job Purpose: Cement Surface Casing			
Well Type: Development Well		Job Type: Cement Surface Casing	
Sales Person: SCOTT, KYLE		Srv Supervisor: MAGERS, MICHAEL	MBU ID Emp #: 339439

Job Personnel

HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #
BORSZICH, STEPHEN A	9	412388	MAGERS, MICHAEL Gerard	9	339439	PONDER, THOMAS Lynn	9	427112
SINCLAIR, DAN J	9	338784						

Equipment

HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way
10001431	60 mile	10724643	60 mile	10872429	60 mile	11259886	60 mile
11360883	60 mile						

Job Hours

Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours
01/02/2012	1	0	01/03/2012	8	1			
TOTAL			Total is the sum of each column separately					

Job

Formation Name	Formation Depth (MD)	Top	Bottom	Form Type	Job depth MD	1119. ft	Job Depth TVD	1119. ft	Water Depth	Wk Ht Above Floor	3. ft	Perforation Depth (MD)	From	To
				BHST										

Well Data

Description	New / Used	Max pressure psig	Size in	ID in	Weight lbm/ft	Thread	Grade	Top MD ft	Bottom MD ft	Top TVD ft	Bottom TVD ft
-------------	------------	-------------------	---------	-------	---------------	--------	-------	-----------	--------------	------------	---------------

Sales/Rental/3rd Party (HES)

Description	Qty	Qty uom	Depth	Supplier
PLUG,CMTG,TOP,9 5/8,HWE,8.16 MIN/9.06 MA	1	EA		

Tools and Accessories

Type	Size	Qty	Make	Depth	Type	Size	Qty	Make	Depth	Type	Size	Qty	Make
Guide Shoe					Packer					Top Plug	9.625	1	HES
Float Shoe					Bridge Plug					Bottom Plug			
Float Collar					Retainer					SSR plug set			
Insert Float										Plug Container	9.625	1	HES
Stage Tool										Centralizers			

Miscellaneous Materials

Gelling Agt	Conc	Surfactant	Conc	Acid Type	Qty	Conc	%
Treatment Fld	Conc	Inhibitor	Conc	Sand Type	Size	Qty	

Fluid Data

Stage/Plug #: 1	Stage Type	Fluid Name	Qty	Qty uom	Mixing Density lbm/gal	Yield ft ³ /sk	Mix Fluid Gal/sk	Rate bbl/min	Total Mix Fluid Gal/sk
Fluid #									

HALLIBURTON***Cementing Job Summary***

1	Fresh Water		20.00	bbl	8.33	.0	.0	.0	
2	VersaCem Lead	VERSACEM (TM) SYSTEM (452010)	160.0	sacks	12.3	2.38	13.75		13.75
	13.75 Gal	FRESH WATER							
3	VersaCem Tail	VERSACEM (TM) SYSTEM (452010)	160.0	sacks	12.8	2.11	11.75		11.75
	11.75 Gal	FRESH WATER							
4	Displacement Fluid		84.00	bbl	8.34	.0	.0	.0	
Calculated Values		Pressures		Volumes					
Displacement	84.2	Shut In: Instant		Lost Returns	0	Cement Slurry	128	Pad	
Top Of Cement	SURFACE	5 Min		Cement Returns	20	Actual Displacement	84.2	Treatment	
Frac Gradient		15 Min		Spacers	20	Load and Breakdown		Total Job	232
Rates									
Circulating	RIG	Mixing	8	Displacement	10/2	Avg. Job	8		
Cement Left In Pipe	Amount	44 ft	Reason	Shoe Joint					
Frac Ring # 1 @	ID	Frac ring # 2 @	ID	Frac Ring # 3 @	ID	Frac Ring # 4 @	ID		
The Information Stated Herein Is Correct				Customer Representative Signature					

The Road to Excellence Starts with Safety

Sold To #: 300721	Ship To #: 2898356	Quote #:	Sales Order #: 9153019
Customer: WILLIAMS PRODUCTION RMT INC - EBUS	Customer Rep: BASCOM, BRENT		
Well Name: RWF	Well #: 511-32	API/UWI #: 05-045-21052	
Field: Rulison	City (SAP): RIFLE	County/Parish: Garfield	State: Colorado
Legal Description:			
Lat: N 39.486 deg. OR N 39 deg. 29 min. 8.621 secs.		Long: W 107.916 deg. OR W -108 deg. 5 min. 3.116 secs.	
Contractor: CYCLONE 17	Rig/Platform Name/Num: CYCLONE 17		
Job Purpose: Cement Surface Casing	Ticket Amount:		
Well Type: Development Well	Job Type: Cement Surface Casing		
Sales Person: SCOTT, KYLE	Srv Supervisor: MAGERS, MICHAEL	MBU ID Emp #: 339439	

Activity Description	Date/Time	Cht #	Rate bbl/min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Crew Leave Yard	01/02/2012 20:00							HES ALL PRESENT
Arrive At Loc	01/02/2012 22:00							HES ARRIVED ON LOCATION 3 HRS EARLY/RIG WAS PULLING DRILL PIPE/RIG CIRCULATED WHILE CASERS RIGGED DOWN AND HES RIGGED UP
Assessment Of Location Safety Meeting	01/02/2012 22:10							TIGHT LOCATION
Pre-Rig Up Safety Meeting	01/03/2012 06:50							JSA ON RIGGING UP
Rig-Up Equipment	01/03/2012 07:00							1 PICKUP 1 ELITE 1 BULK TRUCK
Safety Huddle	01/03/2012 07:50							RIG CREW AND HES ALL PRESENT
Start Job	01/03/2012 08:07							TD-1119 TP-1114 SJ-44 MW-9.3 CSG- 9 5/8 32.3# H-40 OH-13 1/2"
Other	01/03/2012 08:08		2	2			70.0	FILL LINES
Pressure Test	01/03/2012 08:10		0.5	0.5			5600.0	PSI TEST OK
Pump Spacer 1	01/03/2012 08:17		3	20			223.0	FRESH WATER
Pump Lead Cement	01/03/2012 08:24		8	67.8			310.0	VERSACEM 160 SKS 12.3 PPG 2.38 FT3/SK 13.75 GAL/SK
Pump Tail Cement	01/03/2012 08:34		8	60.1			248.0	VERSACEM 160 SKS 12.8 PPG 2.11 FT3/SK 11.75 GAL/SK
Activity Description	Date/Time	Cht	Rate bbl/min	Volume bbl		Pressure psig		Comments

Sold To #: 300721

Ship To #: 2898356

Quote #:

Sales Order #:

9153019

SUMMIT Version: 7.2.27


Friday, January 06, 2012 04:02:00

Cementing Job Log

		#		Stage	Total	Tubing	Casing	
Shutdown	01/03/2012 08:42							
Drop Plug	01/03/2012 08:47							PLUG AWAY NO PROBLEMS
Pump Displacement	01/03/2012 08:48		10	84.2			410.0	FRESH WATER/USED 40 LBS OF SUGAR
Slow Rate	01/03/2012 08:57		2	74			231.0	GOT 20 BBLs OF CEMENT TO SURFACE
Bump Plug	01/03/2012 09:02		2	84.2			250.0	BUMPED PLUG
Check Floats	01/03/2012 09:03			84.2			822.0	FLOATS HELD/GOT .5 BBL BACK
End Job	01/03/2012 09:05							HAD GOOD CIRCULATION THROUGHOUT JOB/THANKS FOR USING HES AND THE CREW OF MIKE MAGERS

WILLIAMS CYCLONE 17 RWF 511-32

SURFACE 9.625

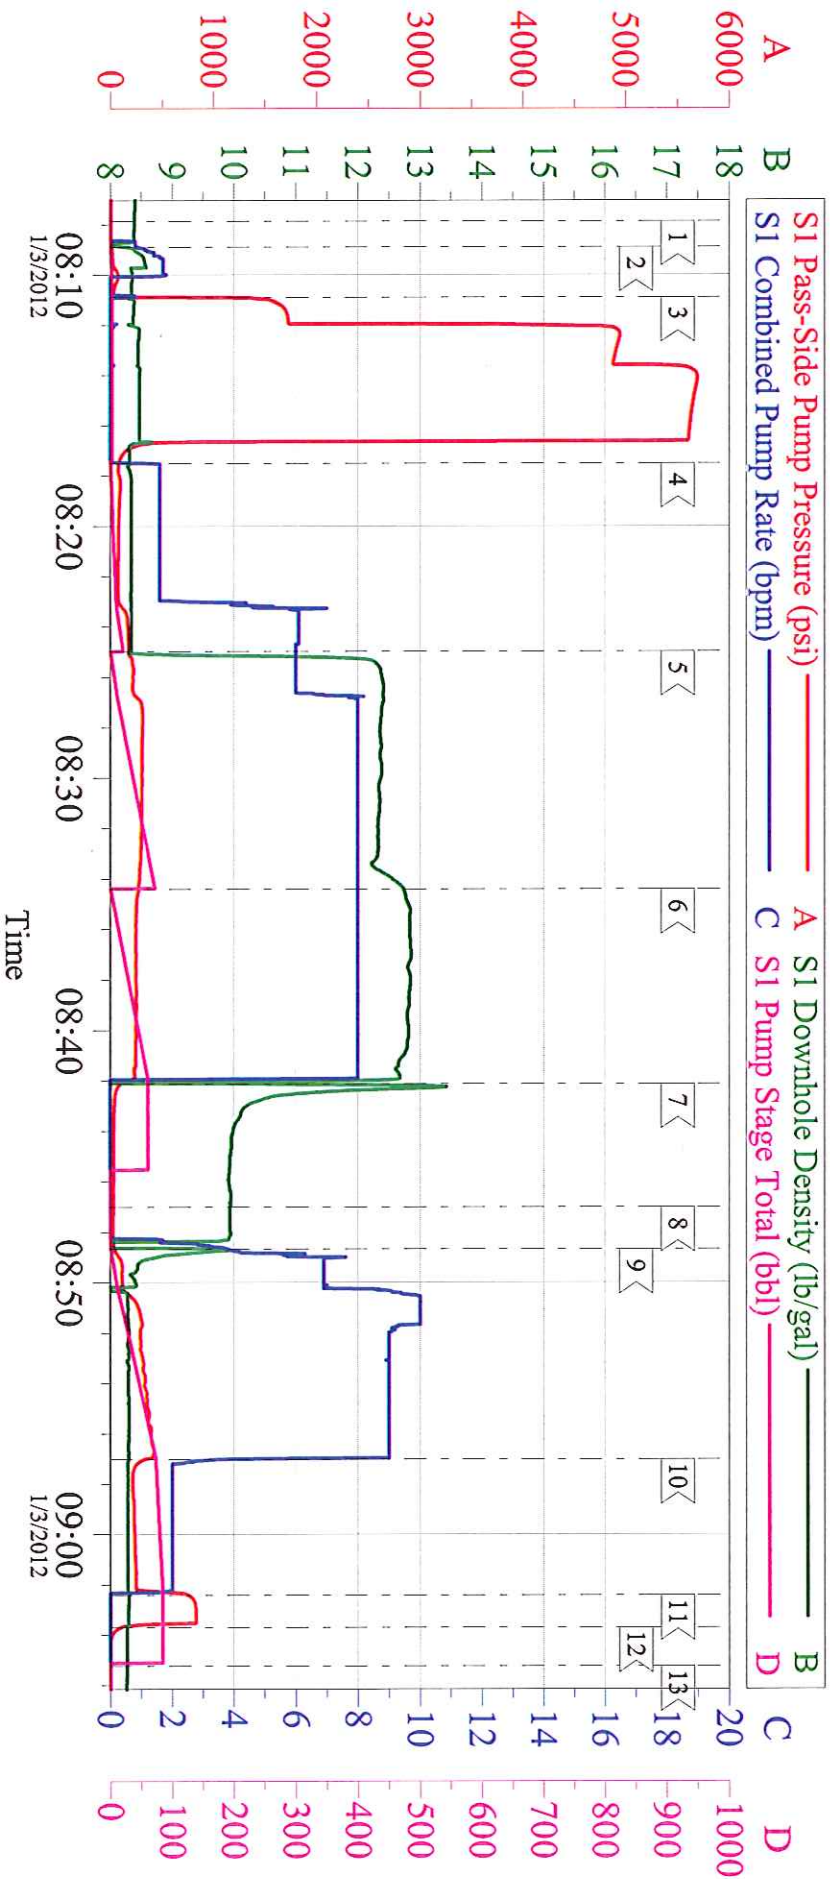


Customer: WILLIAMS CYCLONE 17
Well Description: RWF 511-32
Company Rep: BRENT BASCOM

Job Date: 03-Jan-2012
Job Type: SURFACE
Cement Supervisor: MIKE MAGERS

Sales Order #: 9153019
ADC Used: YES
Elite # 7 STEVE BORSZICH

WILLIAMS CYCLONE 17 RWF 511-32

SURFACE 9.625

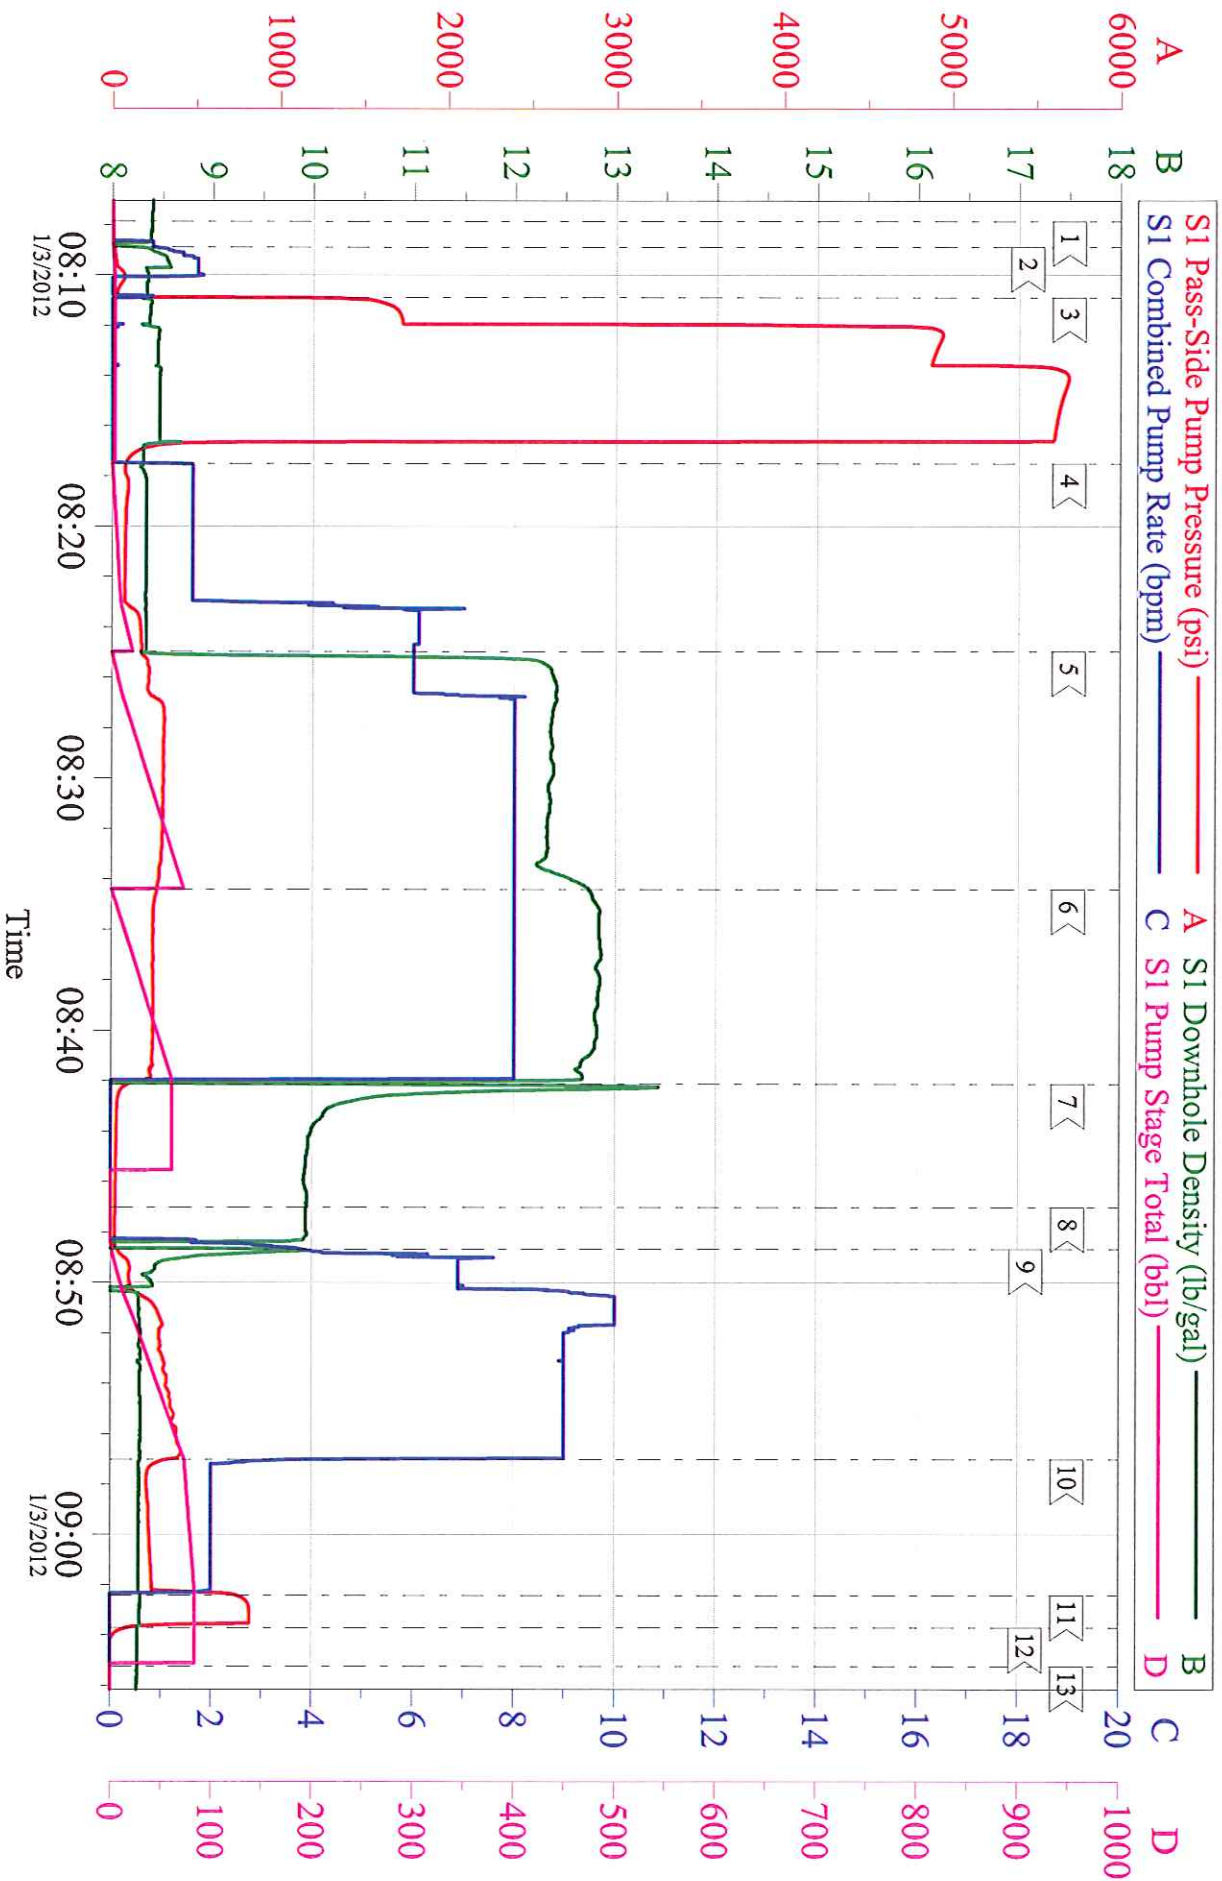

Customer:	WILLIAMS CYCLONE 17	Job Date:	03-Jan-2012	Sales Order #:	9153019
Well Description:	RWF 511-32	Job Type:	SURFACE	ADC Used:	YES
Company Rep:	BRENT BASCOM	Cement Supervisor:	MIKE MAGERS	Elite #	7
					STEVE BORSZICH
