NOBLE ENERGY INC.

Huwa 11-01
S2SW 11-4N-65W
660' FSL & 1980' FWL
WELD COUNTY, CO
Wattenberg
CURRENT WELLBORE SCHEMATIC
with PROPOSED P&A
10/14/2015

API: 05-123-11428
COGCC #

GL Elev: 4690'
KB Elev: 4705'

Spud Date: 10/17/1983

Surface Casing :
8-5/8" 24# @ 351'
Cement: 150 sx
TOC: Surface

TOC @ 6375'

Nio Top 6738'

Production Casing :
4-1/2" 11.6# K-55 @ 7149'
Cement: 160 sx
TD: 10/21/1983

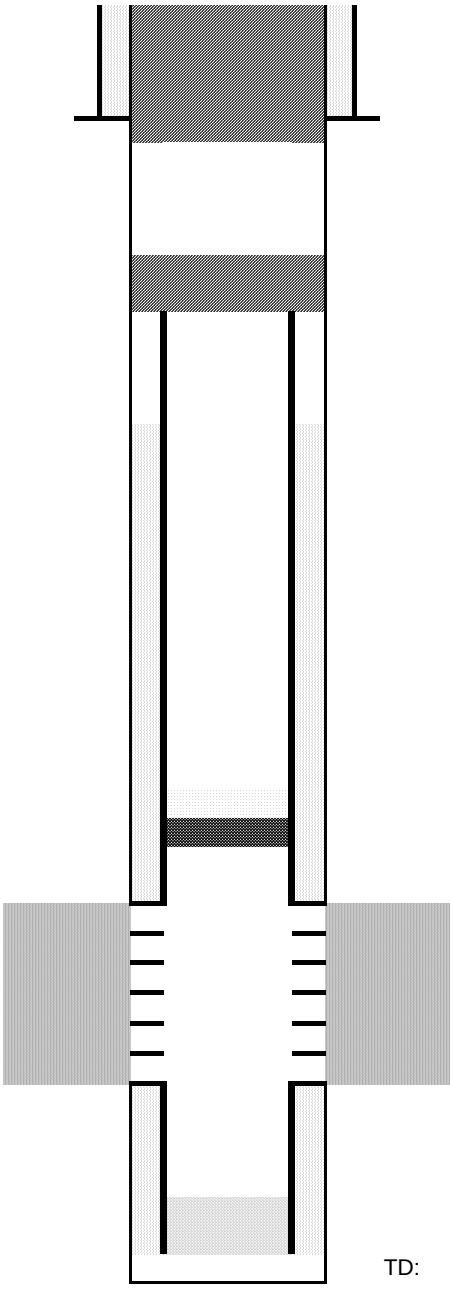

Cut surface casing off 6'-8' below surface.

Pump approx 145 sx shoe plug @ 451'
Will bring cement to surface.

Cut csg @ 4500'
Pump 150 sx stub plug @ 4500'

CIBP @ 6691' w/ 2 sx cement on top

Niobrara Perforations 6741' - 6848'

Codell Perforations 7032' - 7042'

TD: 7150'
